Ping Lite Commercial LEO Station: Conceptual Design and Engineering Plan

Version 0.2: single-Starship-launch architecture, revised against NASA CLDC Final RFP 80JSC027R0004

Prepared for Joshua Almeida

18 October 2026

- How to read this document
  - What changed from v0.1
- 0. Baseline assumptions (change these first)
- 1. Mission and requirements
  - 1.1 Mission statement
  - 1.2 Top-level requirements (v0.2)
- 2. Orbit selection and rationale
  - 2.1 Drag at 420 km (v0.2 single-core station)
- 3. Architecture and layout
  - 3.1 Architecture choice
  - 3.2 Configuration
- 4. Structures and pressurized volume
  - 4.1 Primary structure
  - 4.2 Pressurized volume
  - 4.3 Is that enough?
  - 4.4 Launch-vehicle fit (Starship)
- 5. Environmental control and life support (ECLSS)
  - 5.1 Approach
  - 5.2 Per-person metabolic loads (planning values, approximate)
  - 5.3 Oxygen loop mass balance (6 crew)
  - 5.4 Water loop and resupply impact
  - 5.5 Atmosphere and leakage
  - 5.6 Logistics resupply (6 crew, estimate)
- 5A. NASA science accommodations (mapped to SOW Table 1.5-1)
- 5B. NASA mission phasing: Mission A, then B, then Standard
- 6. Power
  - 6.1 Architecture
  - 6.2 Array sizing
  - 6.3 Battery sizing
- 7. Thermal control
- 8. GNC, propulsion and reboost
- 9. Communications and data
- 10. Crew safety, radiation and debris protection
- 11. Launch, deployment and activation
- 11A. Crew and cargo transportation
- 11B. ISS relationship and transition
- 12. Mass and power budgets
  - 12.1 Mass budget (tonnes, all estimates)
  - 12.2 Power budget (orbit-average, EOL)

- 13. Cost and schedule
  - 13.1 Cost: rough order of magnitude (2026 US$, ±50% or worse)
  - 13.2 Schedule options (honest feasibility)
- 13A. Teaming and past-performance strategy
- 13B. Funding model aligned with NASA's service-based payments
- 14. Key risks and open trade studies
  - 14.1 Top risks (L = likelihood, C = consequence, 1–5)
  - 14.2 Open trade studies
- 15. Next steps
- 16. NASA requirements compliance matrix (v0.2, preliminary)
  - Appendix A. Key equations and constants
  - Appendix B. Reference figures and their status (v0.2 additions)

How to read this document

This is the **second concept iteration** of **Ping Lite** (project working name; the public repository is `new-space-station`). Version 0.1 (18 Oct 2026, kept unchanged in `docs/`) used a five-module station launched on five Falcon rockets. **v0.2 changes the architecture to one large, pre-integrated core station launched on a single Starship flight.** This is the same approach Starlab has publicly announced. v0.2 also closes the main gaps against NASA's Commercial LEO Destination Contract (CLDC) Final RFP, solicitation 80JSC027R0004 (released 9 Oct 2026). The five-Falcon modular design is kept as a documented fallback (Section 14.2, trade T1).

Every number is an **engineering estimate** unless it is labelled as a published figure, and published figures name their source. RFP references give the section and page of the local copies in `refs/`. RFP pages are the printed page numbers, and SOW pages are "Page X of 55". Nothing here claims any real agreement with any company or agency. Partners are described only by type.

What changed from v0.1

Area	v0.1	v0.2	Section
Launch architecture	5 elements on 5 launches (3 Falcon Heavy + 2 Falcon 9), assembled in orbit	**1 integrated core station on 1 Starship launch**, outfitted on the ground; deployable arrays and radiators	3, 11
Permanent crew (berths)	4 (8 peak)	**6: 4 government + 2 commercial** (10 peak for 30 days or less)	0, 1
Pressurized / habitable volume	≈485 / ≈265 m³	**≈560 / ≈305 m³**	4
Orbit-average power at end of life (EOL)	≈35 kW (12 kW payloads)	**≈55 kW capability against a 50 kW design target** (18 kW payloads: 8 NASA + 10 commercial)	6, 12
Solar arrays	4 wings × 75 m²	**6 wings × 75 m²** (same wing design)	6
Radiators	≈175 m²	**≈265 m²** (3 deployable wings + body-mounted)	7
Mass	≈84 t total across 5 launches	**≈93 t launch mass in one launch**, including 25% growth allowance (≈86 t if consumables are offloaded)	12

Area	v0.1	v0.2	Section
Docking ports	3 IDSS docking + 4 berthing	**4 IDSS docking + 2 CBM-type berthing**	3
Science	“≥12 racks”	**Mapped to NASA Table 1.5-1 Category 3:** 58 locker locations (40 heritage-compatible), 3 rack-equivalent spaces, 12 powered payloads, 150 CTBE, 150 L cold stowage, vacuum/O_2/N_2 ports, glovebox, workbench	5A
First launch	≈2033 baseline	**Planning baseline: Q4 2032. Compressed option: Q4 2030 (low likelihood)**	13
Cost to full capability	$4–6 B	**≈$4–7 B** (ROM)	13
New sections	—	Mission A, B and Standard phasing; transport; teaming and past performance; NASA-aligned funding; compliance matrix; ISS relationship and transition	5B, 11A, 11B, 13A, 13B, 16

0. Baseline assumptions (change these first)

#	Assumption	v0.2 baseline value	Why	Sensitivity if changed
A1	Owner/operator	Private U.S. commercial operator. NASA buys services under CLDC (CLINs 1–5); others are commercial customers	CLDC is service-based (SOW §1.0, p. 6)	High: NASA certification scope
A2	Orbit	Circular, 420 km nominal (400–450 km band), 51.6°	Section 2 (unchanged)	High
A3	Permanent crew	**6 = 4 USG + 2 commercial**	NASA may buy up to 4 USG crew (SOW §3.3, p. 51); 2 extra berths keep commercial capacity	High: ECLSS, volume, logistics
A4	Peak crew	**10 for 30 days or less** (6 + one 4-seat crew vehicle)	Handover and visitors	Medium
A5	Uses	NASA research (Category 3), commercial research and manufacturing, private astronauts, Earth observation	—	Medium
A6	Design life	15 yr primary structure; replaceable arrays, batteries and ECLSS units	—	Medium

#	Assumption	v0.2 baseline value	Why	Sensitivity if changed
A7	Launch vehicle	**One Starship (SpaceX)**, standard 9 m fairing class, single launch, no on-orbit assembly. Fallback: modular design on Falcon Heavy, New Glenn or Vulcan (T1)	Single integrated launch; no assembly risk	**Very high:** Starship payload capability, payload-bay configuration and NASA launch-category status are not yet proven (R1–R3)
A8	Station envelope	Pressure shell ≈7.2 m outer diameter / ≈7.0 m inside; ≈7.6 m over MMOD shields; ≈17 m stowed length	Fits Starship's published 8 m payload dynamic envelope (Section 4.4)	High
A9	Crew transport	**Crew Dragon** (certified for ISS under CCtCap) baseline. The station accepts any IDSS crew vehicle, including others certified or in certification for ISS as of 1 Oct 2026	SOW §2.17.1 (p. 38): first 4 increments must use previously certified vehicles	High: single-provider risk
A10	Cargo	**Cargo Dragon** (docking) and **Cygnus** (berthing), both under CRS. Other CRS vehicles if their status allows	SOW §2.17.7 (p. 43): dissimilar redundancy is expected	Medium
A11	Cabin atmosphere	101.3 kPa, ≈21% O_2	Unchanged	Low–medium
A12	Safety and certification	Design to CLDP-REQ-1130 Rev D (J-03, RFP p. 145) and certify per CLDP-PLN-2000 (SOW §2.13, p. 29). Two-fault tolerance against catastrophic hazards where practical	CLDC requirement. Library documents not yet reviewed (open item)	High
A13	Program start	Company-funded Phase A from Jan 2027; CLDC award assumed Apr 2027 ("Spring 2027" per NASA)	RFP §L.9 (p. 278)	Schedule
A14	Margins	25% mass growth allowance (MGA) on dry mass; 15–30% power contingency plus system margin	Normal for concept stage	—

1. Mission and requirements

1.1 Mission statement

Ping Lite will provide a continuously crewed, commercially operated station in low Earth orbit that meets NASA's Standard Service Mission (4 crew including at least 2 USG, 6-month increments,

Category 3 utilization). It will carry **6 permanent crew (4 government + 2 commercial)** and up to 10 for short periods. The station launches fully outfitted on **one launch**.

1.2 Top-level requirements (v0.2)

ID	Requirement	Value	Rationale / NASA trace	Verification
SR-01	Crew capacity	**6 continuous; 10 for 30 days or less**	SOW §1.2 (≥4 incl. ≥2 USG), §3.3 (up to 4 USG)	Analysis, demo
SR-02	Design life	≥15 yr structure; ≥10 yr replaceable units	A6	Analysis, test
SR-03	Orbit	400–450 km, 51.6°	Section 2	Analysis
SR-04	Pressurized volume	**≥540 m³**	≥25 m³ habitable per person at a peak of 10 (Section 4.3)	Inspection
SR-05	Habitable volume	**≥280 m³**	As above	Inspection
SR-06	Continuous power (EOL, orbit-average)	**≥50 kW**, of which ≥8 kW is NASA utilization and ≥10 kW commercial payloads	Section 12.2	Analysis, test
SR-07	Water recovery	≥95% at first crew, rising to ≥98%	5.4	Test
SR-08	O_2 recovery from CO_2	≥45%	5.3	Test
SR-09	Ports	**4 IDSS docking ports** (3 crew vehicles + 1 cargo at the same time) **+ 2 CBM-type berthing ports** (berthed cargo, growth)	Handover at 10 crew needs 3 crew vehicles docked; SOW §2.17.7	Inspection
SR-10	Lifeboat coverage	Docked return seats ≥ crew on board, at all times	Safety	Ops verification
SR-11	Hazard tolerance	Per CLDP-REQ-1130; two-fault tolerant or design-for-minimum-risk	A12	Analysis
SR-12	MMOD	Probability of no critical penetration ≥0.95 over 10 yr (target)	—	Analysis
SR-13	Reboost	Hold altitude through solar maximum without visiting-vehicle reboost	—	Analysis
SR-14	Collision avoidance	≥1 m/s within 24 h of a warning	—	Test
SR-15	Communications	≥1 Gbps payload downlink; ≥95% TT&C coverage; voice, video and telemetry to NASA facilities	SOW §2.16.9.1	Test
SR-16	EVA	Integrated airlock for 2-person EVA	—	Demo

ID	Requirement	Value	Rationale / NASA trace	Verification
SR-17	**NASA utilization**	**Meet Table 1.5-1 Category 3 at Standard Service; Category 1 at Mission A** (Section 5A)	SOW §1.5 (pp. 8–11)	Inspection, test
SR-18	Launch compatibility	**One Starship launch.** Station inside the 8 m diameter payload dynamic envelope; stowed length ≤ the confirmed usable height (≤22 m extended volume per the Starship Users Guide); launch mass ≤ performance confirmed by SpaceX to the insertion orbit	A7, A8	Analysis, launch-vehicle ICD
SR-19	End of life	Controlled deorbit capability	SOW §2.11.5	Analysis
SR-20	Radiation	NASA-STD-3001 limits; storm shelter ≥10 g/cm²	—	Analysis
SR-21	Leak rate	≤0.05% of cabin air mass per day (target)	—	Test
SR-22	**Continuous presence**	USG crew gaps of no more than 14 days at handovers	SOW §1.7.2 (p. 12)	Ops
SR-23	**Commander autonomy**	Commander can undock the crew vehicle without ground support; recovery operations without communications	SOW §1.8.1.1 (p. 13)	Training, demo
SR-24	**Transport capability per mission (Category 3)**	Pressurized up 100 CTBE; trash 50; return 50; 4 powered lockers each way; conditioned stowage 70 L up / 70 L down	SOW Table 1.5-1 (p. 10)	Analysis, ops
SR-25	**Internal pressure isolation**	At least one pressure-tight internal bulkhead/hatch zone plus node isolation, so a leak does not force abandoning the whole station (single-volume risk, R6)	New for the single-core design	Analysis, test

2. Orbit selection and rationale

Unchanged from v0.1: **420 km circular, 51.6°**, with a 400–450 km band. This keeps compatibility with ISS-certified crew and cargo vehicles and with ISS ascent, abort and recovery planning. Starship's published reference performance is quoted for orbits up to 500 km and up to 98.9° (Starship Users Guide v1.0, 2020), so 420 km / 51.6° is within the stated range. **Exact performance to a 51.6° insertion orbit must be obtained from SpaceX** (the guide says to contact sales for specific orbits).

2.1 Drag at 420 km (v0.2 single-core station)

Station plus up to three docked vehicles ≈125 t (estimate). Ram-facing area ≈500 m² (conservative, dominated by 6 array wings). C_D = 2.2, v = 7,657 m/s.

Case	Density ρ (estimate)	Drag F	Δv per year	Biprop (Isp 300 s)	Hall EP (Isp 1,500 s)	EP power at 60 mN/kW
Solar mean	4×10^{-12} kg/m³	0.13 N	33 m/s	1.4 t/yr	0.28 t/yr	2.2 kW
Solar max (high)	1.5×10^{-11} kg/m³	0.48 N	122 m/s	5.2 t/yr	1.04 t/yr	8.1 kW

Orbit geometry is unchanged: period 93.0 min, longest eclipse ≈36 min, sunlight ≈57 min, ≈5,650 battery cycles per year.

3. Architecture and layout

3.1 Architecture choice

Baseline: a single integrated core station, "Ping Lite Core", launched once on Starship. It is a 7.2 m diameter aluminium pressure vessel with five internal decks, a forward docking node, and an aft service section. The aft section carries propulsion, stowed solar wings, stowed radiators and the robotic arm. Everything is integrated and tested on the ground. In orbit, the station deploys its arrays, radiators and arm, completes uncrewed activation and checkout, and is then ready for its first crew.

Why single-launch (changed from v0.1):


1. **No on-orbit assembly.** This removes v0.1 risks R5 (berthing/arm failure before modules are joined) and the 10–12 month assembly campaign.
2. **Ground integration and test of the whole station.** Interfaces are verified end to end before launch, which helps certification (CLDP-PLN-2000).
3. **Fewer pressurized interfaces.** One primary pressure vessel replaces five, so there are fewer CBM seals and leak paths.
4. **Category 3 hardware from day one.** NASA capability phasing (Mission A, then B, then Standard) becomes a matter of certification and operations, not launches.
5. **Precedent:** Starlab has publicly chosen a single Starship launch for a ≈7.7 m diameter, ≈17 m tall, ≈400 m³ station (Starlab website and one-pager, checked Oct 2026).

What it costs: the whole station rides on one launch (R2), it depends on Starship maturity and payload-bay accommodation (R1, R3), large-diameter tooling and facilities are needed, and a single pressure volume needs internal isolation (R6, SR-25).

3.2 Configuration

Zone	Size (estimate)	Main functions
Forward node	≈2.6 m diameter × 2.5 m	1 axial IDSS (crew vehicle #1), 2 radial IDSS (crew vehicles #2/#3), 2 radial CBM-type berthing ports (berthed cargo such as Cygnus; growth module). Pressure-tight hatch to the core (isolation zone)
Forward dome	7.0 m, 2:1 elliptical head	Logistics stowage; translation to the node; zenith window
Deck 5 (Wardroom)	7.0 m Ø × 2.2 m	Galley and wardroom for 10, 4 visitor/handover crew quarters, 3rd hygiene station, cycle ergometer, large Earth-viewing window
Deck 4 (Habitation)	7.0 m Ø × 2.2 m	**6 permanent crew quarters** (water-walled storm shelter), 2 hygiene stations, treadmill + resistive exercise device, crew medical station
Deck 3 (Commercial lab)	7.0 m Ø × 2.2 m	Commercial payload racks, manufacturing bays (furnace, bioprinting), 2nd (commercial) glovebox, science airlock with slide table
Deck 2 (NASA lab)	7.0 m Ø × 2.2 m	NASA Category 3 accommodations (Section 5A): locker carriers, 3 rack-equivalent spaces, NASA glovebox, workbench, cold stowage, vacuum/O_2/N_2 ports
Deck 1 (Systems)	7.0 m Ø × 2.2 m	ECLSS racks, avionics, power conversion, **integrated EVA airlock** (crew lock with outward hatch through the barrel; 2 suits), pressure-tight bulkhead to Deck 2 (isolation zone 2)
Aft dome	2:1 elliptical head	NASA bulk stowage (150 CTBE) and logistics; tunnel to the aft port
Aft service section (unpressurized)	≈7.6 m Ø × ≈3 m	Biprop + Hall propulsion and tanks; 4 CMGs; 2 deployable array booms with alpha joints, 6 roll-out wings (stowed); 3 deployable radiator wings; ammonia pump modules; batteries; **aft IDSS** (cargo, reboost, propellant transfer) through a tunnel; robotic arm stowed; Starship payload adapter interface

Decks are 2.2 m tall, the same deck height Starlab has publicly shown (SpaceNews, mockup reporting). The barrel circumference (≈22 m at 7.0 m inside diameter) gives about **16 usable rack bays per lab deck** at ≈1.05 m pitch (estimate), leaving room for hatches and the central translation path.

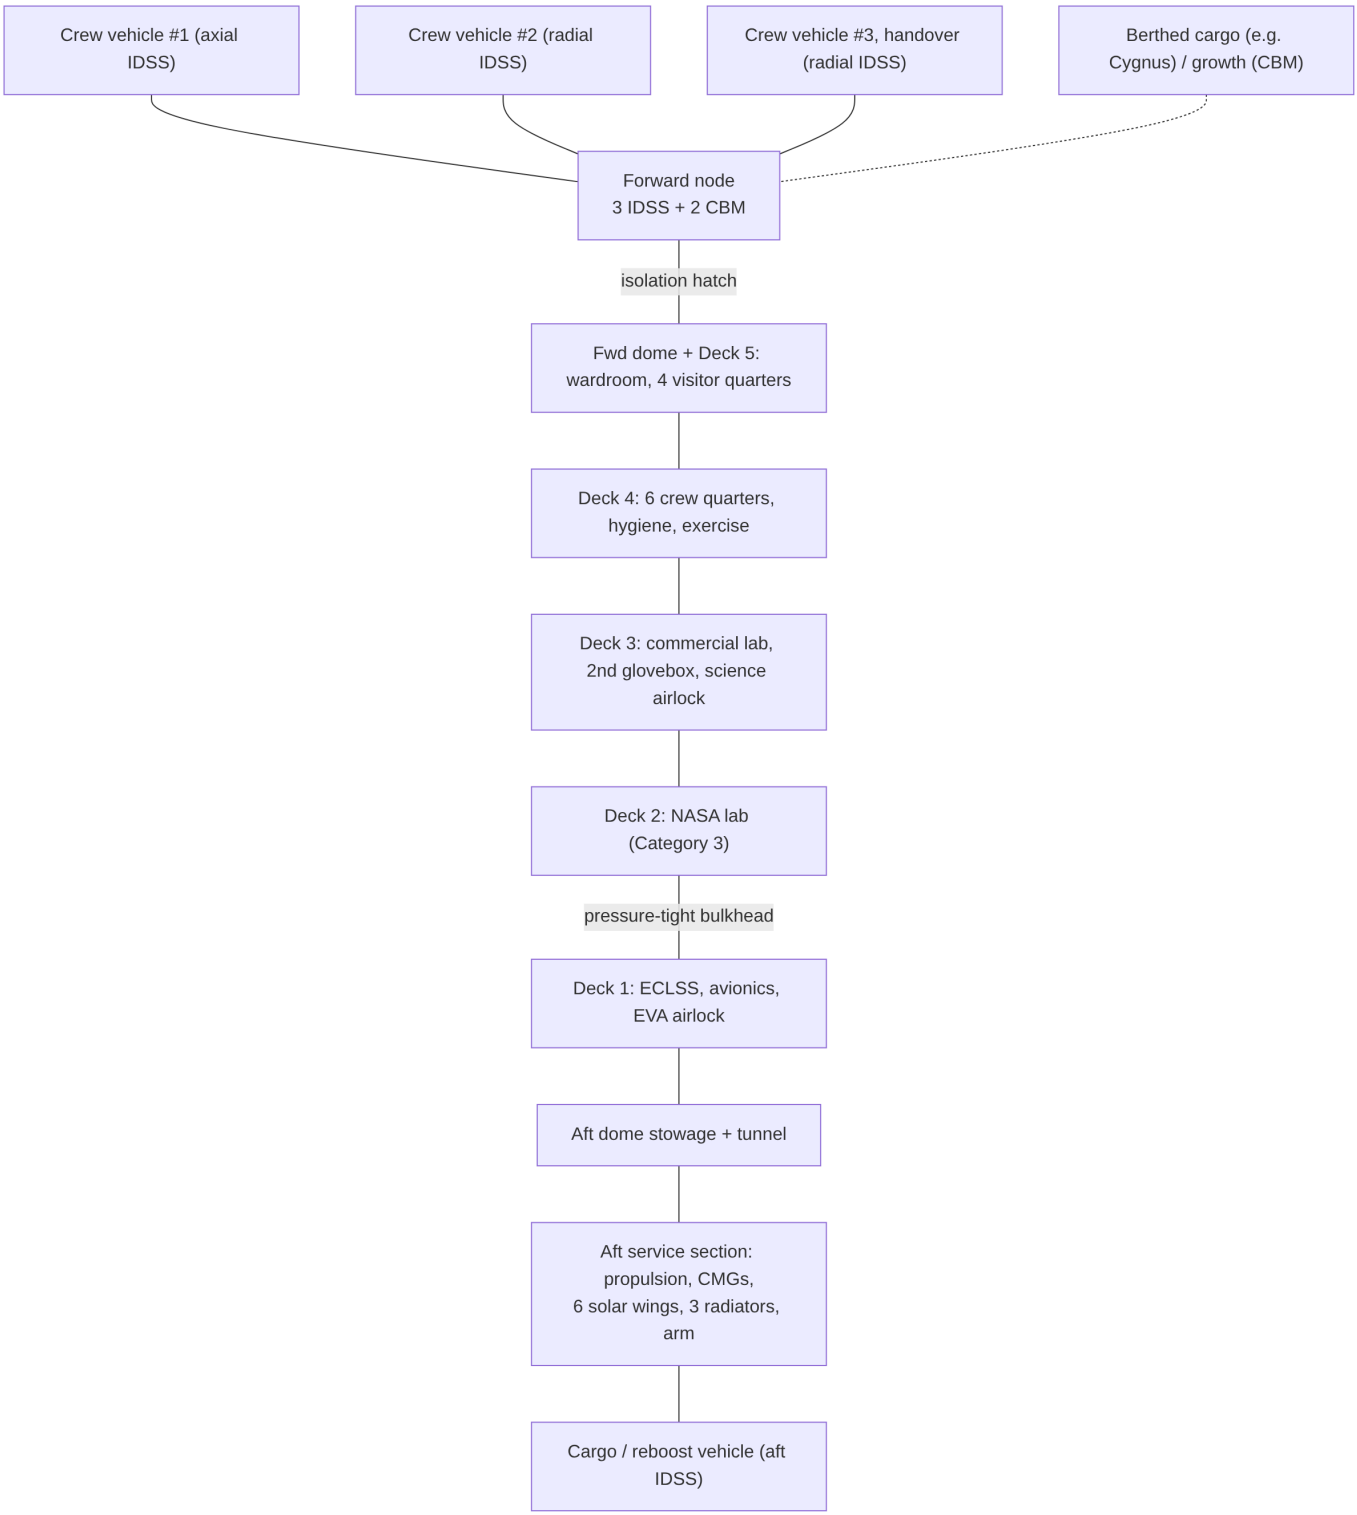

Flight attitude: long axis along the velocity vector, node forward. Array booms extend port and starboard and track the Sun with alpha joints and beta gimbals. Radiators fly edge-on to the Sun. The station flies near torque-equilibrium attitude.

4. Structures and pressurized volume

4.1 Primary structure

- **Material:** welded aluminium 2219 or Al-Li 2195 with orthogrid barrel panels, forged rings, 2:1 elliptical domes, and internal deck beams. Large-diameter (≈7 m) welding and tooling are

needed (new facility; cost line in 13.1).

- **Design pressure:** MEOP 104 kPa; ultimate factor 2.0 (confirm against CLDP-REQ-1130 and its referenced standards, e.g. ANSI/AIAA S-080, J-03 p. 145).
- **Pressure-only check at r = 3.5 m:** $t_{min} = \frac{104\,\text{kPa} \times 3.5\,\text{m} \times 2.0}{270\,\text{MPa}} \approx 2.7\,\text{mm}$. Launch loads (the station is carried in Starship on a mission-unique adapter), fracture control and pressure cycling drive the design to an equivalent skin of ≈7–8 mm (estimate).
- **Shell area:** barrel π × 7.1 × 12 ≈ 268 m², domes ≈100 m², total ≈370 m². At ≈21 kg/m² equivalent that is ≈7.8 t. Rings, domes, hatches, launch interface and thrust structure bring primary structure to ≈12 t, plus ≈5.5 t of secondary structure (decks, rack frames, partitions). All estimates.
- **MMOD:** stuffed Whipple shields on ≈370 m² at ≈10 kg/m² ≈ 3.7 t.

4.2 Pressurized volume

Zone	Geometry	Volume (estimate)
Barrel	7.0 m ID × 12.0 m (5 decks)	≈462 m³
Two 2:1 elliptical domes	(2/3)π r² (r/2) each	≈90 m³
Forward node	≈2.0 m ID × 2.5 m	≈8 m³
Total pressurized		**≈560 m³**
Habitable (≈55% of pressurized, estimate)		**≈305 m³**

4.3 Is that enough?

- Using the common ≈25 m³ per person planning guideline: 6 crew need 150 m³, and a peak of 10 needs 250 m³. **≈305 m³ gives ≈51 m³ per person at 6 crew, and ≈22% margin at a peak of 10.**
- NASA Category 3 utilization takes ≈18 m³ of wall volume on Deck 2, and NASA's 150 CTBE needs ≈10 m³ of stowage envelope in the aft dome (Section 5A). This is outfitting volume, so it is already outside the habitable fraction.

Station	Pressurized	Habitable	Source/status
ISS	≈916 m³	≈388 m³	NASA facts
Starlab	≈400 m³	—	Starlab website/one-pager, Oct 2026: 7.7 m × 17 m, 4 continuous / 8 at turnover, single Starship launch, 2029
Vast Haven-1	80 m³	45 m³	Vast (as in v0.1)
Ping Lite v0.2	**≈560 m³ (est.)**	**≈305 m³ (est.)**	—

4.4 Launch-vehicle fit (Starship)

- **Published figures (Starship Users Guide v1.0, March 2020):** 9 m outer-diameter fairing; **8 m diameter payload dynamic envelope**; an **extended payload volume for payloads up to 22 m tall**; **100+ t to LEO** in the fully reusable configuration (orbits up to 500 km, up to 98.9°). The guide shows payload deployment by **opening a clamshell fairing door and tilting the payload and adapter** before separation.
- **Demonstrated so far (public reporting, checked Oct 2026):** 2026 Starship test flights carried payloads of order **35–40 t** (e.g. ≈37.5 t reported for Flight 12, May 2026). The 100 t class is the Block 3 design figure, **not yet demonstrated**.
- **Ping Lite fit:** ≈7.6 m over shields gives ≈0.2 m radial clearance to the 8 m envelope. ≈17 m stowed length is inside the 22 m extended volume (≈5 m margin, subject to the actual nose-

taper geometry). Launch mass ≈93 t (Section 12.1) is **≈93% of the 100 t design figure and about 2.5× what has been demonstrated**.

- **Open risks (R3):** (1) whether a ≈7.6 m × 17 m single payload can leave through the standard clamshell door, or needs a mission-unique large door, a jettisonable nose or another deployment method; (2) the actual usable height in the nose taper; (3) the payload adapter and the loads into a crewed pressure vessel; (4) performance to 51.6°; (5) payload-bay environments (acoustics, thermal, contamination). All need a SpaceX payload ICD early in Phase A.

5. Environmental control and life support (ECLSS)

5.1 Approach

The approach is unchanged from v0.1: ISS-class regenerative ECLSS from the first crew, with dissimilar backups. It is now sized for **6 continuous / 10 peak**. There are two CO_2 removal units, each sized for 6 crew. The O_2 generator is sized for 6 crew continuously, with stored O_2 for peaks. The water processor is sized for 24+ kg/day. Fire detection is fitted per deck, and the isolation zones are described in SR-25.

5.2 Per-person metabolic loads (planning values, approximate)

O_2 0.84; CO_2 1.04; drinking + food-prep water 2.5; hygiene ≈1.5; food ≈1.8 (kg/person/day). Unchanged from v0.1.

5.3 Oxygen loop mass balance (6 crew)

1. O_2 needed: 6 × 0.84 = **5.04 kg/day**.
2. Electrolysis water: 5.04 × 36/32 = **5.67 kg/day**, which yields 0.63 kg H_2/day (315 mol).
3. CO_2 produced: 6 × 1.04 = **6.24 kg/day**.
4. Sabatier (H_2-limited): 315 mol H_2 react with 78.75 mol CO_2 (3.47 kg). This produces **2.84 kg H_2O/day** and 1.26 kg CH_4/day (vented).
5. Closure: 2.84 / 5.67 = **50%**. 2.77 kg CO_2/day is vented.
6. Electrolysis power: 5.04 kg/day × ≈30 MJ/kg ≈ **1.75 kW** average.

5.4 Water loop and resupply impact

- Water processed: 6 × ≈4 = **24 kg/day**. A 98% recovery rate loses ≈0.5 kg/day. Including O_2 make-up and the offsets from food and metabolic water, **net water resupply is ≈1.5–3 kg/day ≈ 0.6–1.1 t/yr** (estimate).
- Open loop would need ≈30 kg/day ≈ 10.8 t/yr. **Regeneration saves ≈10 t/yr of upmass.**

5.5 Atmosphere and leakage

Cabin air ≈560 m^3 × 1.2 kg/m^3 ≈ 670 kg. At 0.05%/day the leak is ≈0.34 kg/day ≈ **123 kg/yr**. On top of that come airlock losses and NASA payload gas use from the O_2/N_2 ports (allocation 50–100 kg/yr, estimate, TBC against CLDP-STD-1106).

5.6 Logistics resupply (6 crew, estimate)

Item	t/yr
Food	3.9
Water (net)	0.9
Gas (N_2/O_2 make-up, EVA, payload gas)	0.6

Item	t/yr
Spares and maintenance	2.6
Crew supplies	0.75
Chemical propellant	1.0
Xenon/krypton	0.3–1.0
NASA utilization upmass	1–2
Commercial payloads	2–4
Total	**≈13–17 t/yr ≈ 4–5 cargo flights/yr** (assumes ≈3–4 t useful pressurized cargo per flight; confirm with providers)

5A. NASA science accommodations (mapped to SOW Table 1.5-1)

NASA's minimum utilization capability (SOW §1.5, Table 1.5-1, pp. 9–11) is stated in Middeck Locker Equivalents (MLE) and Cargo Transfer Bag Equivalents (CTBE). The Category 3 total of **58 locker locations = 34 locker-style + 3 rack-equivalent volumes × 8 MLE** (note 5: a rack equivalent is 4 vertical × 2 horizontal MLE, contiguous). **40 of the 58 must be compatible with NASA heritage lockers** per CLDP-STD-1102 (note 1). Resource allocations below are **estimates to be confirmed against CLDP-STD-1106 and CLDP-REQ-1130**, which we have not yet obtained (Q11, Q12 in the questions draft).

NASA item (Category 3)	NASA minimum	Ping Lite v0.2 provision	Location	Volume impact (est.)	Power allocation (est., orbit-average)
Reconfigurable locker locations	58 total	**58 for NASA:** 5 locker-carrier bays × 8 MLE = 40 positions (34 to NASA, 6 commercial) + 3 rack-equivalent bays (24 MLE)	Deck 2	8 bays ≈ 13.6 m³ wall envelope	34 lockers ≈1.7 kW; 3 rack-eq ≈3.0 kW
Heritage-compatible lockers	40 of 58	**All 40 locker-carrier positions** use CLDP-STD-1102 interfaces (34 NASA + 6 commercial). The 3 rack-equivalent bays can also take heritage lockers. Whether those count toward the 40 is open (Q10)	Deck 2	—	—
Rack-equivalent volumes	3 (8 MLE each)	3 dedicated bays with power, data, cooling, and vacuum/gas drops	Deck 2	in the row above	in the row above
Deployable pressurized powered payloads	12	**12 utility outlet panels** (power + data). 8 on Deck 2/workbench, 4 on Decks 3/5	Decks 2, 3, 5	negligible (aisle use)	12 × 0.1 ≈1.2 kW

NASA item (Category 3)	NASA minimum	Ping Lite v0.2 provision	Location	Volume impact (est.)	Power allocation (est., orbit-average)
CTBE stowage	150	**150 CTBE** dedicated NASA stowage (≈8 m³ of bags, ≈10 m³ envelope incl. racks)	Aft dome	≈10 m³	—
Vacuum resource access	2	2 ports (high-vacuum line, valved, through the barrel)	3 rack-eq bays	small	—
Vacuum exhaust access	3	3 ports (separate exhaust line)	rack-eq bays + workbench	small	—
Gaseous O_2 / N_2	2 / 2	2 + 2 ports from station tanks, co-located with vacuum exhaust in ≥1 rack bay (note 2)	rack-eq bays	small	—
Potable water access	Yes	Payload water dispenser on Deck 2	Deck 2	—	—
Conditioned stowage	150 L total (≥100 frozen, ≥50 refrigerated)	**≈170 L:** 1 cold-stowage rack (≈100 L at −80 °C class + ≈50 L at +4 °C) + 2 powered double-locker freezers (≈20 L, −20 °C) as spare and transfer capacity	Deck 2	1 bay + 2 locker positions	≈1.2 kW
Workbench	1 (NASA use 50%)	1 fold-down workbench bay with 4 outlets, vacuum exhaust, imaging	Deck 2	1 bay	≈0.2 kW
Glovebox	1 (NASA use 100%)	**1 NASA-dedicated glovebox + 1 commercial glovebox** (because NASA expects 100% use, SOW Table 1.6-1)	Decks 2, 3	2 bays	NASA ≈0.5 kW
Total NASA allocation		**11 of ≈16 Deck 2 bays + aft-dome stowage**		**≈18 m³ wall + ≈10 m³ stowage**	**≈7.8 → 8.0 kW allocated**

Transport side (Category 3, per mission, SR-24): 100 CTBE up, 50 trash, 50 return, 4 powered lockers each way, and 70 L conditioned up and down. These are carried by Cargo Dragon (pressurized up/down with return) and Cygnus (up and trash disposal), using powered-locker and cold-bag services from the transport provider (to be confirmed in LOIs).

Categories 1 and 2: the station carries Category 3 hardware from launch. Mission A uses a subset of it (≥3 lockers, 2 of them heritage-compatible, 4 powered payloads, 20 CTBE, 20 L frozen). Mission B

uses ≥20 lockers, 1 rack-equivalent, 8 powered payloads, 45 CTBE and 60 L conditioned stowage. The difference between categories is **certification and logistics, not hardware**.

5B. NASA mission phasing: Mission A, then B, then Standard

Phase	Configuration	Crew	Duration	Utilization	Enabled by
Uncrewed activation & checkout (A&C)	Full station, deployed	0	≈1–2 months after launch	—	Launch + deployments
Mission A (crew-tended), CLIN 3A	Full station, operated crew-tended	**3 (2 USG + 1 contractor commander)**	**1 month**	Category 1 (subset of installed hardware)	Interim certification milestone (J-11 allows interim milestones to order Mission A, RFP p. 184). The first NASA increment includes A&C objectives (SOW §3.3, p. 50)
Mission B (continuous), CLIN 3B	Full station	4 (≥2 USG)	6 months	Category 2	Certification for continuous crew
Standard Service, CLIN 3C	Full station	4 USG (2–4 bought by NASA)	6 months	Category 3	System Certification Review
6-crew full commercial operations	Full station	6 (4 USG + 2 commercial), 10 peak	continuous	Category 3 + commercial	Logistics cadence of 4–5 cargo flights/yr

The Mission A configuration needs: 1 Crew Dragon docked (4 seats for 3 crew), the HAB deck plus 1 lab deck activated, ECLSS in regenerative mode with 30 days of stored O_2/water reserve, and ≈15 kW of load against ≈68 kW orbit-average at beginning of life (BOL). Per J-17 assumptions (RFP p. 261), **no more than 2 Mission A/B missions may come before Standard Service, and no more than 2 missions per year are allowed**. Ping Lite therefore plans **1 Mission A and at most 1 Mission B**, then Standard Service.

6. Power

6.1 Architecture

Six roll-out solar wings of the same design as v0.1 (75 m² active area each, ROSA/iROSA-type), on two deployable booms with alpha rotary joints and per-wing beta gimbals. Two-axis tracking is required at 51.6° (β up to ≈75°). Li-ion batteries in N+1 strings. 120 Vdc main bus plus a high-voltage converter for the Hall thrusters.

6.2 Array sizing

Design target **50 kW orbit-average at EOL**: 38.7 kW demand including contingency, plus system margin (Section 12.2).

$P_{SA} = \frac{50 \times 36.0/0.75 + 50 \times 56.9/0.90}{56.9} \approx 97.7\,\text{kW}$ in sunlight at EOL, which needs 97,700 / 237 W/m² ≈ **412 m²**. **Baseline: 6 wings × 75 m² = 450 m².**

	BOL	EOL (15 yr)
Array output, sun-pointed	≈134 kW	≈107 kW
Orbit-average power	≈68 kW	**≈55 kW**

Per-m² values are unchanged from v0.1 (297 W/m² BOL, 237 W/m² EOL). All 6 wings deploy at launch, so the reduced-power initial configuration that v0.1 needed is no longer required.

6.3 Battery sizing

50 kW × 36 min = 30 kWh delivered, or 33.3 kWh from the cells (0.9 efficiency). At ≤30% depth of discharge that is 111 kWh. With one string of five failed: **≈139 kWh, so 140 kWh nameplate**. At ≈130 Wh/kg that is **≈1.08 t** (estimate).

7. Thermal control

Architecture unchanged: water internal loops, ammonia external loop, interface heat exchangers outside the cabin. Heat to reject is ≈50 kW electrical + 1.5 kW metabolic (10 crew peak) + environment, giving a **design value of 57 kW**. At 290 W/m² for a two-sided panel that needs 197 m², or **≈246 m²** with +25% margin. **Baseline: 3 deployable radiator wings × 75 m² + ≈40 m² body-mounted on the service section and barrel = ≈265 m².** The radiators are stowed against the service section for launch (deployment risk R8).

8. GNC, propulsion and reboost

- **CMGs:** 4 × ≈1,800 N·m·s (estimate; v0.1 had 1,200). The single body plus 6 wings gives ΔI ≈ 6–8×10⁶ kg·m² (estimate). The gravity-gradient torque at a 5° offset is ≈2–2.7 N·m, so the station must fly torque-equilibrium attitude. Cyclic momentum is of order 1,000–1,300 N·m·s.
- **Hall EP:** 2 operating + 1 spare thrusters of ≈4.5 kW. Solar mean needs 2.2 kW and 0.28 t/yr of propellant. **Solar max needs ≈8.1 kW**, so both thrusters run near full power. Trade T4 looks at a 3rd operating thruster.
- **Biprop:** ≈3.0 t initial load. Annual Δv ≈16 m/s × 125 t / 2,943 ≈ 0.68 t, plus docking RCS ≈0.3 t, gives **≈1.0 t/yr**. Refuelling uses the aft IDSS port's propellant coupling (R9). Visiting-vehicle reboost is the backup.
- **Deorbit:** ≈108 m/s from 420 km for an ≈86 t station needs ≈3.2 t of high-thrust propellant. Baseline: a dedicated deorbit vehicle or tug procured near end of life.
- **Navigation and comms:** unchanged from v0.1 (dual GNSS; optical relay ≥1 Gbps; Ka backup; S-band TT&C with ≈26 dB margin). Voice, video and telemetry interfaces to NASA facilities are added (SOW §2.16.9.1).

9. Communications and data

Unchanged from v0.1 Section 9, plus: payload data and command interfaces to NASA's payload operations (as described in RFP L.17.3.1 TA.1 C&DH content, p. 298), an archive of all commands, telemetry, voice and video for the contract period (SOW §2.16.9.1), and separate NASA and commercial payload networks.

10. Crew safety, radiation and debris protection

- **Lifeboats:** 6 crew means 2 Crew Dragons docked (8 seats). A handover at 10 crew means 3 crew vehicles (12 seats) on the 3 node IDSS ports, with cargo on the aft port.
- **Depressurisation (single volume):** for a 1 cm² hole, τ = 670 kg / 0.014 kg/s ≈ 13.3 h, and the **time to fall to 70 kPa is ≈4.9 h** (≈30 min for 10 cm²). In v0.1 a leaking module could be closed off. **Here the main volume is one vessel**, so v0.2 adds two pressure-tight isolation zones (node and Deck 1 bulkhead, SR-25), leak location by acoustic sensors, and a patch kit. Evacuation to the docked crew vehicles remains the final control (R6).
- **Radiation, MMOD, medical:** as v0.1. The storm shelter uses the water-walled crew quarters on Deck 4.
- **Fire:** detection per deck; ventilation shutoff per deck; isolation zones.

11. Launch, deployment and activation

Step	Vehicle	Event	Time from launch (estimate)
L1	**Starship**	Ping Lite Core launched fully integrated (≈93 t, or ≈86 t with consumables offloaded) to an insertion orbit; separation by mission-unique adapter and door/deploy method (R3)	0
D1	—	Own propulsion raises the orbit to 420 km; array booms, 6 wings, 3 radiators and the arm deploy; ECLSS and thermal start-up	+1 to +14 days
C0	Cargo Dragon	First cargo: consumables and items offloaded for mass margin, propellant top-up via the aft port (if offloaded)	≈+1 month
A&C	—	Uncrewed activation and checkout complete	≈+1–2 months
C1	Crew Dragon	**Mission A: 3 crew, 1 month** (first NASA increment includes A&C objectives)	≈+2–3 months
—	Crew/Cargo Dragon, Cygnus	Mission B or Standard Service; then 6-crew operations	≈+6–12 months

Launch count: 1 station launch (v0.1: 5). After that the station receives only crew and cargo flights.

11A. Crew and cargo transportation

The plan uses **ISS-certified vehicles only for the first 4 NASA increments** (SOW §2.17.1, p. 38: certified, or in certification, for ISS under CRS or CCtCap as of 1 Oct 2026).

Role	Primary	Alternate (status to be verified before proposal)	Port
Crew	**Crew Dragon** (CCtCap, operational)	Other CCtCap vehicle if it meets the “previously certified” definition	IDSS (node axial/radial)
Cargo with return (Type 1)	**Cargo Dragon** (CRS)	—	IDSS (any)
Cargo without return / disposal (Type 2)	**Cygnus** (CRS)	Other CRS vehicles per their status	CBM-type berthing via the arm (node)
Station launch	**Starship** (one flight)	Fallback: modular design (T1)	—

- **Traffic model at 6 crew (estimate):** crew flights 4/yr (2 NASA rotations of 4 USG crew; 2 commercial rotations of 2 long-duration crew + up to 2 short-stay customers), and cargo flights 4–5/yr.
- **GFTSS:** NASA may provide up to 2 crew and 4 cargo flights per year for the first 4 increments (SOW §2.17.3, p. 39), but no more than 1 crew and 2 cargo flights per increment (J-15, p. 259). Ping Lite prices **end-to-end service with GFTSS as an option** for the first 4 increments. The commercial rotations are always contractor-provided, because GFTSS is not offered for private astronaut missions (SOW p. 40).
- **Redundancy:** IDSS and CBM ports allow dissimilar crew and cargo vehicles (SOW §2.17.7). Stored consumables cover ≥6 months without resupply at 4 crew.
- **Required at proposal:** Letters of Intent from each crew and cargo transport provider covering flight rate, capability and pricing (RFP L.17.3.1 TA.1(5)(B), p. 299). **None exist yet.**

11B. ISS relationship and transition

Source for all ISS facts and numbers in this section: `trade-save-iss.md` (19 Oct 2026), which cites NASA, GAO, OIG and ESA documents. **Ping Lite does not propose to save, boost, take over or dock with the ISS.** The proposal treats NASA’s plan as fixed: last ISS crew departs mid-2030, US Deorbit Vehicle (USDV) reentry notionally Jan 2031 (trade-save-iss §1). Ping Lite’s planning launch is Q4 2032, so on the baseline the two stations never overlap.

ISS-extension compatibility (unpriced, ≈½ page in the proposal).

- Ping Lite flies at **420 km / 51.6°** (Section 2), the same inclination as the ISS and within its altitude band (≈415 km). It uses the same **IDSS docking and CBM-type berthing** interfaces and the same ISS-certified crew and cargo vehicles (Crew Dragon, Cargo Dragon, Cygnus; Section 11A).
- GAO reports that NASA will decide in **2027** whether to launch the USDV in 2029 or extend ISS operations, and NASA says the USDV can wait on the ground during an extension (trade-save-iss §1, §4.1).
- **If NASA extends the ISS to ≈2032–33**, Ping Lite could overlap with it. Possible uses: crew handover with no gap in continuous presence, shared crew and cargo traffic planning, and moving small NASA hardware between the stations by visiting vehicle. Ping Lite needs **no added hardware** for this, and the offer depends on nothing NASA has not already planned.
- Ping Lite does **not** depend on an extension. It also has **no** propulsive proximity-operations capability to dock with the ISS. Adding one is not proposed (trade-save-iss option O7: not feasible on the baseline schedule).

Option 1: host legacy ISS research hardware (optional, priced separately if NASA asks). Ping Lite offers to accept NASA-owned ISS research hardware that has been returned to the ground, or stored on Axiom’s PPTM. NASA asked for PPTM partly to save ISS equipment (trade-save-iss §5, O5). This would use the 40 heritage-compatible locker positions (Section 5A, CLDP-STD-1102) and the 3

rack-equivalent bays, subject to recertification for Ping Lite power, data and thermal interfaces. **Cost and the list of eligible hardware are to be determined** (no estimate yet).

Option 2: early flight-software demonstration before mid-2030 (optional). The early demo is **software only**: Ping Lite flight software runs on a computer already hosted on the ISS (or on Axiom's), before the last ISS crew leaves in mid-2030. It flies no Ping Lite hardware and needs no second spacecraft. A dedicated bridge element was assessed and rejected (trade-save-iss O8: estimate $100–300 M for even a small demo element). Sources are listed in trade-save-iss Appendix A (S21–S29).

Proven ways to fly software on the ISS:

Host	What it has shown	Source
HPE Spaceborne Computer-2 (SBC-2), via ISS National Lab	Open to proposals; containerised code is built on the ground and pushed to orbit; a Kubernetes (k3s) AI workload deployed by `git push` ran on 24 Jul 2025	HPE; ISS National Lab; BruhnBruhn
Axiom AxDCU-1 (Red Hat Device Edge / MicroShift)	On ISS since CRS-33 (Aug 2025), with remote updates, automated rollback and self-healing; the larger AxODC Node ISS is planned for 2027	ISS National Lab; Axiom; TechRadar
Voyager (formerly Nanoracks) LEOcloud Space Edge micro datacenter, Bishop airlock and external platform	RHEL 10.1 deployed on the ISS unit (May 2026); hosted-payload power, data and mission ops as standard services; software-only SHIRE simulation environment	Voyager; Red Hat/Voyager
AWS Snowcone (Ax-1, 2022)	Stock device passed the NASA safety review in about 7 months; operated remotely over SSH; a 7 GB model was uplinked mid-mission	AWS; GeekWire

Software to test (flown in monitor-only or "shadow" mode, never commanding the ISS):

1. **ECLSS control and fault detection, isolation and recovery (FDIR):** run the Ping Lite algorithms against live ISS data and compare their detections with the actual events. Public ISS telemetry is streamed openly (ISSLive / Lightstreamer). Detailed ECLSS data would need a NASA data agreement (TBD).
2. **Autonomous operations and crew-off station management:** run the planner and the safing logic through the station's real communication gaps and loss-of-signal periods. This is the case Ping Lite needs between increments (SR-22) and in crew-tended Mission A.
3. **Power and thermal scheduling:** the Section 6–7 load scheduler, fed with real orbit, beta-angle and eclipse data.
4. **Avionics software stack:** the operating system and container image, deployment pipeline, update and rollback, and radiation-upset logging, run on the hosted computer.

What it proves for CLDC:

- **On-orbit evidence for software management and assurance:** SOW §2.10.3 (Software Management Plan, DRD CLDC-107) and §2.11.2 (p. 24: software safety and assurance plan meeting the intent of NASA-STD-8739.8B, plus third-party IV&V).
- **Practice with the payload software path:** SOW §2.15.4 (p. 32).
- **Early data toward human rating:** flight ECLSS and power-control software is Class A under the NPR 7150.2 definition ("required to sustain a safe, habitable environment"). The demo does **not** certify that software, but it gives flight data for FDIR performance and for the assurance case.

- **Past performance:** a flown Ping Lite product before 2030, from a team with no flight record today (Section 13A).

Rough schedule (estimate):

When	Step
Q1–Q2 2027	Pick the host and submit a proposal (HPE SBC-2 via ISS National Lab, Axiom, or Voyager)
2027–2028	Develop the software and test it on the ground against recorded and public ISS telemetry
2028–2029	Host safety and integration review. Snowcone's took about 7 months; a software-only load on an existing host is expected to be shorter, but that is not confirmed
2029 to mid-2030	Flight runs, finishing before the last ISS crew departs. Continue on Axiom's computers after that if available

Cost: TBD. No host publishes a price for this service. The bridge-element figure above does not apply to this option.

Not included: ISS boost to a storage orbit, commercial takeover of the US segment, legacy-module reuse and return of modules to Earth. NASA's 2024 analysis rejected all of them, and trade-save-iss rates them low feasibility (§5, O3–O6).

12. Mass and power budgets

12.1 Mass budget (tonnes, all estimates)

Item	Dry CBE
Primary structure (shell, domes, rings, launch interface)	12.0
Secondary structure (5 decks, rack frames, partitions)	5.5
MMOD shielding	3.7
Forward node + 4 IDSS + 2 CBM-type	2.6
Propulsion (dry)	1.4
GNC (4 CMGs, sensors)	1.2
Avionics & comms	2.0
Power (6 wings + gimbals 5.4, 140 kWh battery 1.1, PMAD 0.9)	7.4
Array booms + 2 alpha joints	3.0
Thermal (internal loops, 3 radiator wings, pumps)	5.5
ECLSS (6 crew / 10 peak)	5.2
Robotic arm	1.5
Crew systems (10 quarters, 3 hygiene, galley, 2 exercise suites)	5.4
Payload infrastructure incl. NASA Category 3, 2 gloveboxes, cold stowage, science airlock, windows	7.0
Stowage racks (incl. 150 CTBE NASA)	1.0
EVA airlock hardware + 2 suits	2.0
Harness & outfitting	2.5
Dry CBE	**68.9**

Item	Dry CBE
MGA (25%)	17.2
Propellant 3.0 + consumables 1.5 + initial cargo 2.0	6.5
Launch mass (with MGA)	**≈92.6 (≈93)**
Launch mass with consumables and cargo offloaded to the first Cargo Dragon	≈86

Launch margin check: 93 t is ≈93% of Starship's 100+ t design figure. That figure is not yet demonstrated, and the inclination penalty for 51.6° is unknown. **Margin is thin to negative until SpaceX confirms performance.** Mitigations: offload up to 6.5 t; burn down MGA as the design matures; insert lower and climb on own propulsion (EP climb time is a trade); fallback T1(b). This is risk R1.

12.2 Power budget (orbit-average, EOL)

Subsystem	CBE (kW)	Contingency	With contingency (kW)
ECLSS (6 crew, incl. electrolysis 1.75 kW)	6.3	20%	7.5
Thermal control	2.5	20%	3.0
Avionics, C&DH, comms	1.8	20%	2.2
GNC	0.8	25%	1.0
Crew systems (6 crew)	3.6	20%	4.3
Robotics	0.4	25%	0.5
NASA utilization allocation (Section 5A)	8.0	—	8.0
Commercial payloads & manufacturing	10.0	—	10.0
Electric propulsion (solar mean)	2.2	—	2.2
Total demand			**38.7**
Capability (EOL)			**≈54.6**
System margin			**≈15.9 kW (41% over demand)**

Solar max: EP rises to 8.1 kW (+5.9), leaving ≈10 kW margin. A 10-crew peak adds ≈2.5 kW, which is within margin. Mission A load is ≈15 kW against ≈68 kW at BOL.

13. Cost and schedule

13.1 Cost: rough order of magnitude (2026 US$, ±50% or worse)


Item	ROM	Notes
Phase A–B (to PDR), incl. risk reduction	$0.35–0.55 B	Large-diameter structural test article starts in Phase B
Phase C–D: design, qualification, flight station, structural and thermal test articles, software, ground segment	$2.5–4.0 B	One integrated vehicle (fewer interfaces) offsets the new large-diameter tooling
Large-diameter manufacturing and integration facility; transport to the launch site	$0.2–0.4 B	8 m class vehicle cannot move by road; waterfront site likely
Launch (1 Starship, mission-unique adapter and deployment hardware)	$0.15–0.4 B	**No public price for this type of mission. Estimate only**
Program reserve (≈20–25%)	$0.65–1.35 B	
Total to operational station	**≈$4–7 B**	v0.1: $4–6 B

Item	ROM	Notes
Annual operations (mission control, sustaining, spares, insurance; excludes crew and cargo transport)	≈$0.4–0.8 B/yr	Transport is priced per provider LOI (TBD)
Optional: launch insurance or a second flight-spare primary structure	TBD	Mitigates R2

13.2 Schedule options (honest feasibility)

NASA's goal is continuous USG presence before the ISS deorbit at the **end of CY2030** (SOW §1.0, p. 6). CLDC CLIN 1 requires **CDR no later than award + 12 months and the Integrated Progress Review (IPR) no later than award + 18 months** (J-11 Table 1, RFP p. 163). With award in spring 2027, that means CDR by about Apr 2028.

Milestone	Compressed option ("buy-not-build", single launch)	Planning baseline
Phase A start (company-funded)	Jan 2027	Jan 2027
CLDC award (assumed)	Apr 2027	Apr 2027
PDR	Q4 2027	Q3 2028
CDR	**Q2 2028 (CA+12, meets J-11)**	Q3 2029 (**misses the J-11 CA+12 limit; needs tailoring, see Q5**)
IPR	Q3–Q4 2028 (CA+15–18)	2029
Structural qualification	2028–2029	2029–2031
Integration and test of the whole station	2029–Q3 2030	2031–Q3 2032
Launch	**Q4 2030**	**Q4 2032**
A&C complete	Q1 2031	Q1 2033
Mission A (3 crew, 1 month)	**Q1 2031**	Q1 2033
Standard Service	H2 2031	H2 2033
6-crew operations	2032	2034

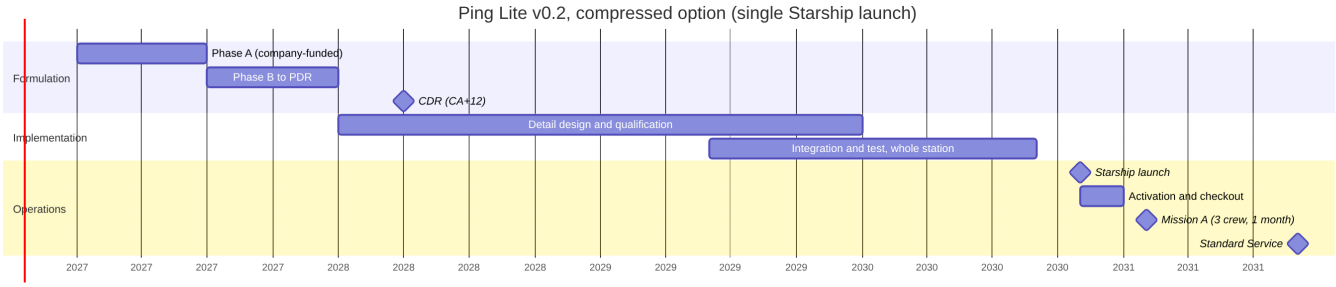

Feasibility assessment (judgment, not analysis):

- **A single integrated launch does help the schedule.** It removes the v0.1 assembly campaign (10–12 months from first launch to full capability) and the need to certify several element interfaces in orbit. The station reaches Category 3 hardware capability on day one.
- **Even the compressed option lands the first crew about 1–3 months after the end-2030 ISS deorbit target**, not before it. It also needs CDR-to-launch in about 30 months for a first-of-a-kind 7 m class crewed station by a new company. For comparison, Starlab, with an experienced team, completed CDR in February 2026 and targets a 2029 launch, which is about 3+ years (v0.1 sources).
- **It also depends on factors outside our control:** Starship reaching ≈90+ t operational performance with a station-sized payload deployment method, and a NASA launch-category

path (SOW §2.17.5), by 2030.

- **Our judgment: the compressed option has a low likelihood (well under 50%; roughly 1-in-5 or less) for a standalone new entrant.** The planning baseline (launch Q4 2032) is the realistic case. Proposing the compressed dates would risk being rated not credible. Proposing the baseline means arriving after ISS, which NASA may rate as a weakness (Q4 in the questions draft).
- **Options to be honest about in the proposal:** (1) bid the baseline with Mission A and Standard Service pricing starting in 2033; (2) bid the compressed option only with an experienced major partner who supplies the pressure vessel and ECLSS heritage; (3) supply Ping Lite elements or subsystems to an established bidder; (4) use the H.5 on-ramp later.

13A. Teaming and past-performance strategy

No agreements exist. This section describes the types of partners needed and why, mapped to what the RFP evaluates.

- **What NASA evaluates:** up to 3 of the prime's own recent contracts plus up to 2 each for up to 5 major team members (≥$100 M of base-period work) (RFP L.17.4(a), p. 313). An offeror with no relevant record gets a **neutral** rating (M.5(b), p. 356). CCSC-2 and CDFF agreements count as relevant (M.5, p. 357). The past performance of a parent or affiliate counts only with "meaningful involvement" (L.17.4(e)). CLIN 1 tests **business maturity** (SOW §3.1, p. 50). Financial capability needs statements, investor commitments, and copies of teaming agreements (L.17.5, pp. 316–318).
- **Implication:** as a new entity, Ping Lite's own rating would be neutral. Credibility has to come from major team members with real work share.

Partner type	Role in Ping Lite	Why it matters to the evaluation
Large-diameter pressurized-structure manufacturer with human-spaceflight heritage	Pressure vessel, domes, MMOD, structural qualification	Highest technical risk; relevant past performance
ECLSS supplier with ISS-class heritage	Regenerative ECLSS racks	Certification heritage; reliability (R5)
Power-system supplier (roll-out arrays, PMAD)	6 wings, booms, alpha joints	Heritage hardware
Launch provider (Starship)	Launch, payload adapter, deployment, ICD	LOI required; R1–R3
Crew and cargo transport providers	Crew Dragon, Cargo Dragon, Cygnus services	LOIs required (L.17.3.1 TA.1(5)(B))
Space robotics supplier	Arm and capture	Buy rather than build (T8)
Mission operations, training and astronaut-services provider	Ops center, training facility (SOW §2.16.9), commander	Operations past performance
Payload integration services company	NASA payload integration (SOW §2.15)	Utilization past performance
AS9100 integration and test facility partner	Whole-station AIT	Business maturity
Small businesses	Subsystems and services	SBU subfactor (Volume II)

Strategy options: (a) Ping Lite as prime with 3–5 major team members, each holding a defined SOW share; (b) a joint venture with an established aerospace company (JV past performance is weighted per M.5(c)); (c) Ping Lite as supplier/subcontractor to an existing CLDC bidder. **Decision needed before about mid-November 2026** so that Volume III (requested 24 Nov 2026) can be written.

13B. Funding model aligned with NASA’s service-based payments

How CLDC pays (RFP sources):

- **IDIQ, firm-fixed-price.** Guaranteed minimum $100 M; ceiling $34.063 B through 2042 (B.8, p. 22). A CLIN 2 award adds a supplement of **4 CLIN 3 service missions, ≥2 of them Standard** (H.32(a), p. 88), with reductions if Standard Service certification is more than 2 years late against the offeror’s committed date (H.32(b)).
- **CLIN 1 and 2 are milestone-paid** (performance-based payments, FAR 52.232-32; total ≤90% of price, L.10, p. 278). J-11 percentage ranges: CBR and PDR 10–20% each, CDR 30–50%, IPR ≥20% of CLIN 1; CLIN 2 DCR ≥20%, System Certification 20%, others ≥5% each (RFP pp. 163, 184–185).
- **CLIN 3 per-mission prices** for 2, 3 and 4 USG crew (end-to-end and CLD-only), with 1 or 2 missions per year. **CLIN 4** add-ons (extra seats, utilization, cargo; NASA has first right of refusal on 50/65/75% of available cargo for 2/3/4 seats, SOW Table 3.4.1-1). **CLIN 5** studies.
- **Fair-market pricing:** NASA’s price must be equitable with commercial and sovereign customers, and NASA money cannot subsidize private or sovereign seats (H.33, p. 89).

Ping Lite funding plan (structure, all estimates):

Phase	Use of funds	Sources
2027–2028 (Phase A to CDR/IPR)	$0.35–0.55 B + early long-lead items	Equity (seed/Series A–B); CLIN 1 milestone payments (amount competitive and not known); partner cost-share
2028–launch (C/D, facility, launch)	$3–5 B	Equity growth rounds; strategic partner in-kind work share; CLIN 2 milestone payments; possibly export-credit or asset-backed debt once certification risk falls; customer pre-payments for commercial berths and lab bays
Operations	$0.4–0.8 B/yr + transport	CLIN 3/4 NASA mission revenue (up to 2 missions/yr); 2 commercial long-duration berths (≈4 seats/yr) + short-stay visitors; ≈10 commercial lab bays and manufacturing; sovereign-astronaut missions at H.33-consistent prices

Key point: NASA’s money arrives mostly as **service payments after certification**. Development is largely privately financed. CLIN 1/2 milestone payments help but are not expected to cover it. The private raise is still the critical path (R4). The 6-berth design exists so that NASA’s 4-seat purchases do not use up all commercial capacity.

14. Key risks and open trade studies

14.1 Top risks (L = likelihood, C = consequence, 1–5)

ID	Risk	L	C	Mitigation
R1	**Starship maturity and performance:** 100 t class not yet demonstrated (≈35–40 t payloads in 2026 tests); 51.6° performance unknown; station launch mass ≈93 t	4	5	Early SpaceX performance quote and ICD; MGA burn-down; offload 6.5 t; keep fallback T1(b) mature to SRR
R2	**Single point of failure at launch:** losing the launch loses the whole station	2	5	Launch insurance; flight-spare primary structure option; full ground qualification
R3	**Payload bay and door constraints:** how an ≈7.6 m × 17 m crewed station is accommodated, loaded and deployed (clamshell door vs. mission-unique door/nose); bay environments; usable height in the nose	4	5	Payload ICD in Phase A; mission-unique adapter study; early design accommodation
R4	**Funding and demand** (≈$4–7 B)	4	5	Phased raise; partners; anchor customers; 6 berths for commercial revenue
R5	**ECLSS reliability** at 6–10 crew	3	4	Dissimilar redundancy; long-duration ground test
R6	**Single pressure volume:** a leak or fire affects the whole habitable volume	3	4	Isolation zones (SR-25); leak location; evacuation to crew vehicles
R7	**NASA launch-vehicle category** (SOW §2.17.5) for Starship by the launch date	3	4	Category 3 plan or Category 2 path with H.26 insurance; question Q15
R8	**Deployment failures** (arrays, radiators, booms): no crew present at deployment	3	4	Redundant actuators; partial-deployment power modes; arm-assisted deployment
R9	**Propellant resupply** interface	3	3	EP for drag; visiting-vehicle reboost
R10	**Schedule versus ISS deorbit**	5	4	Compressed option; partnering; honest baseline

ID	Risk	L	C	Mitigation
R11	**Past performance / business maturity** (new entity)	4	4	Major team members (13A)
R12	**Crew transport single provider**	3	5	IDSS for any vehicle; consumables reserve
R13	**Large-diameter manufacturing facility and transport** to the launch site	3	3	Waterfront site; early facility trade

14.2 Open trade studies

ID	Trade	Options	Status
T1	**Launch architecture**	**(a) v0.2 baseline: single integrated core on 1 Starship. (b) Fallback: modular design on Falcon-class vehicles**, resized for 6 crew (see below). (c) 2–3 large modules on New Glenn (7 m fairing)	(a) baseline; (b) kept mature to SRR
T2	Orbit	51.6°/420 km vs 45°/450–500 km	Unchanged
T3	Habitat construction	Rigid aluminium vs expandable	Unchanged
T4	Reboost	2+1 vs 3+1 Hall thrusters vs chemical only	Solar-max power
T5	External coolant	Ammonia vs non-toxic	Unchanged
T6	ECLSS closure	ISS-class vs higher O_2 closure	Unchanged
T7	Cabin pressure	101.3 vs ≈70 kPa	Unchanged
T8	Robotic arm	Buy vs build	—
T9	Bus voltage	120 vs ≈300 Vdc (larger 55 kW system now favours a study)	Elevated
T10	Transport ownership	End-to-end vs GFTSS for the first 4 increments	New pricing input
T11	Launch mass margin	Offload consumables; lower insertion orbit and EP climb; reduce MGA	New

T1(b) fallback, the v0.1 modular design resized for v0.2 requirements (estimates): 6 elements (Core-Node, Habitat, Lab, Airlock, enlarged Power & Thermal Truss, plus a new Logistics & Habitation Module) on **6 launches (5 Falcon Heavy + 1 Falcon 9)**, ≈110 t total with MGA, ≈615 m³ pressurized / ≈340 m³ habitable, 6 wings × 75 m², ≈55 kW EOL. First crew would come after launch 2, with Mission A on the Core + Habitat. It needs a 10–12 month assembly campaign and extended Falcon fairings (v0.1 risk R2). Cost ≈$5–8 B (ROM). It avoids Starship dependence but adds assembly risk and launches.

15. Next steps

Next 30 days

1. **By Wed 21 Oct 2026, 2:00 p.m. ET:** Joshua reviews and submits the clarification questions (`nasa-questions-draft.md`) to jsc-cldc@mail.nasa.gov.
2. Request CLDC Technical Library access (CLDP-REQ-1130 Rev D, CLDP-STD-1102/1106, CLDP-PLN-2000) and fill the TBCs in Section 5A.
3. **Decide by about 31 Oct 2026** whether to request any Government Task Agreements (due 22 days after release).
4. Approach SpaceX for a Starship performance estimate to 51.6° and a payload accommodation/ICD discussion (R1, R3).
5. **Decide the bid posture** (prime / JV / supplier) and start partner outreach (13A).

Before 8 Dec 2026 (if bidding): Volume III past performance (requested 24 Nov), transport and launch LOIs, J-11 and J-12 work plans, J-17 mission plan, L-07 business case, and the IMS.

---

16. NASA requirements compliance matrix (v0.2, preliminary)

Status key: **Meets** = the design provides it on paper (not yet verified); **Partial** = provided with open items; **Gap** = not met or not yet addressed; **TBD** = requires documents we have not seen.

#	NASA requirement	Source (section, page)	Ping Lite v0.2 response	Status
1	≥4 total crew incl. ≥2 USG (Standard)	SOW §1.2, p. 7	6 continuous (4 USG + 2 commercial)	Meets
2	Up to 4 USG crew purchasable (B/Standard), 3 (A)	SOW §3.3, p. 51	4 USG berths; Mission A 3 crew	Meets
3	Continuous crew, ≤14-day gap	SOW §1.7.2, p. 12	Overlapping handovers; 3 crew-vehicle ports	Meets
4	Mission A: 3 crew / 2 USG / 1 month / Category 1	SOW Table 3.3.1, p. 53	Section 5B	Meets
5	Mission B: 4 / 2 / 6 months / Category 2	SOW Table 3.3.2, p. 53	Full station	Meets
6	Standard: 4 / 2 / 6 months / Category 3	SOW Table 3.3.3, p. 53	Full station	Meets
7	Assembly plan from Category 1 to 3	SOW §1.2, p. 7; L.17.3.1 TA.1(2)(D), p. 297	Single launch; phasing by certification (5B)	Meets
8	58 locker locations, 40 heritage-compatible	SOW Table 1.5-1 note 1, pp. 9–10	34 + 3×8; 40 heritage positions	Partial (Q10)
9	3 rack-equivalent volumes	Table 1.5-1, note 5	3 dedicated bays	Partial (interface TBD, Q10)
10	12 deployable powered payloads	Table 1.5-1	12 outlet panels	Partial (power per location TBD, Q11)
11	150 CTBE stowage	Table 1.5-1	150 CTBE, aft dome	Meets

#	NASA requirement	Source (section, page)	Ping Lite v0.2 response	Status
12	Vacuum resource 2 / exhaust 3 / O_2 2 / N_2 2, co-located	Table 1.5-1, note 2	Provided at rack-equivalent bays	Partial (CLDP-STD-1106 TBD)
13	Potable water access	Table 1.5-1, note 6	Dispenser on Deck 2	Meets
14	150 L conditioned stowage (100 frozen, 50 refrigerated)	Table 1.5-1, note 3	≈170 L	Meets (temperature ranges TBD)
15	Workbench (50%), glovebox (100%)	Table 1.5-1; Table 1.6-1, p. 11	1 workbench; NASA glovebox + commercial glovebox	Meets
16	Transport per mission: 100/50/50 CTBE, 4 powered lockers, 70 L conditioned each way	Table 1.5-1, p. 10	Cargo Dragon + Cygnus	Partial (needs provider LOIs)
17	First 4 increments on previously certified crew/cargo vehicles	SOW §2.17.1, p. 38	Crew Dragon, Cargo Dragon, Cygnus	Meets
18	GFTSS option and traffic model	SOW §2.17.3, p. 39; J-15, p. 259	Priced as an option; Section 11A	Partial (Q8)
19	Accommodate ≥1 crew + ≥1 cargo provider; dissimilar redundancy should be supported	SOW §2.17.7, p. 43	4 IDSS + 2 CBM-type	Meets
20	Crew launch from a U.S. site; CONUS / U.S.-waters landing	SOW §2.17.6, p. 43	Crew Dragon	Meets
21	Element launch on an NLS Category 3 vehicle (Category 2 with approval)	SOW §2.17.5, p. 42	Starship. **Current NLS category status not verified**	**Gap / TBD (R7, Q15)**
22	Cargo launch vehicles with ≥3 successful flights of a similar configuration	SOW §2.17.5, p. 42	Falcon 9 (Dragon), Cygnus launcher per CRS	Meets (verify)
23	U.S. commercial provider; domestic source	RFP H.8; L.17.5(b)(3), p. 316	U.S. company; supplier nationality controls	Partial (corporate set-up)
24	Certification per CLDP-PLN-2000; requirements CLDP-REQ-1130 Rev D	SOW §2.13, p. 29; J-03, p. 145	Plan to comply; library access pending	**TBD**
25	CLIN 1: CDR ≤ CA+12 months, IPR ≤ CA+18 months	J-11 Table 1, p. 163	Compressed option meets; baseline does not	**Partial / Gap (Q5)**
26	Activation & Checkout in the first NASA increment	SOW §3.3, p. 50	Uncrewed A&C + Mission A	Meets
27	Commander can undock without ground; recovery without communications	SOW §1.8.1.1, p. 13	Contractor commander, trained	Meets (training plan TBD)

#	NASA requirement	Source (section, page)	Ping Lite v0.2 response	Status
28	Control centers: commands, telemetry, voice/video to NASA; archive	SOW §2.16.9.1, p. 37	Section 9	Meets
29	High-fidelity training facility	SOW §2.16.9.2, p. 37	Partner (13A)	Partial
30	Public affairs: ≥4 minor events/month; ≥7 major events/mission	SOW §2.23, p. 49	Ops plan	Meets (plan TBD)
31	Orbital debris, deorbit	SOW §2.11.5	Controlled deorbit (8)	Partial
32	Past performance volume	L.17.4, p. 313	Team-member strategy (13A)	**Gap** (new entity)
33	Financial capability; teaming arrangements	L.17.5(b)(4), pp. 316–318	Funding plan (13B); no agreements	**Gap**
34	Transport and launch LOIs	L.17.3.1 TA.1(5)(B), p. 299	None yet	**Gap**
35	Fair market pricing; no subsidy of private/sovereign seats	H.33, p. 89	Pricing policy (13B)	Meets (policy)
36	Standard Service commitment date (H.32 Table H.32.1)	H.32, p. 88	H2 2031 compressed / H2 2033 baseline	Decision needed

Appendix A. Key equations and constants

As in v0.1: $\mu = 3.986\times10^{14}$ m³/s²; $R_E = 6{,}378$ km; $g_0 = 9.81$ m/s²; $\sigma = 5.67\times10^{-8}$ W/m²K⁴; solar constant 1,361 W/m². Orbital velocity $\sqrt{(\mu/a)}$; drag $\tfrac{1}{2}\rho v^2 C_{DA}$; hoop stress pr/t; radiator $\eta\varepsilon\sigma(T_r^4 - T_{sink}^4)$; SMAD array sizing.

Appendix B. Reference figures and their status (v0.2 additions)

Figure	Value	Source type
Starship fairing / payload envelope	9 m OD fairing; 8 m dynamic envelope; extended volume to 22 m height; 100+ t to LEO (reusable, ≤500 km, ≤98.9°); clamshell-door deployment	Starship Users Guide v1.0 (SpaceX, March 2020). May be superseded; confirm with SpaceX
Starship demonstrated payload	≈35–40 t class on 2026 test flights (≈37.5 t reported, Flight 12, May 2026)	Public reporting (Wikipedia summary), checked Oct 2026; secondary source
Starlab	7.7 m × 17 m; ≈400 m³; 4 continuous / 8 at turnover; 35 kW; 500 km / 45°; single Starship; 2029; 130 MLE; 2.2 m deck height	Starlab website/one-pager; Voyager; SpaceNews; checked Oct 2026
CLDC requirements	As cited by section and page	Local copies of Final RFP, SOW J-01, Summary of Changes (`refs/`)
All other numbers	Engineering estimates	This document
